

LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Automated Rubric Assignment Evaluator

Name: G Ganikhasri

SRN: PES1UG24AM098

Section: B

1. Lab Objective

The objective of Lab 2 is to use Jira to turn functional requirements into Agile backlog items, simulate sprints, and analyse progress.

This lab builds on the functional requirements identified in Lab 1 for the Automated Rubric Assignment Evaluator.

2. Agile Backlog

The Jira backlog was organized into two Epics and six User Stories.

2.1 Epics

Epic	Jira Key	Description
Evaluation Results Review	ARAE-1	Enable Faculty Evaluators to access evaluated submissions and review test results, rubric score breakdown, and total evaluation score.
Evaluation Status Handling	ARAE-2	Handle unavailable evaluation results and inform the evaluator that the submission may still be under evaluation.

2.2 User Stories and Story Points

Key	User Story	Epic	Story Points	Priority / Ordering
ARAE-3	View Evaluated Submissions	Evaluation Results Review	2	Core functionality; placed in Sprint 1
ARAE-4	Retrieve Evaluation Results	Evaluation Results Review	2	Core functionality; placed in Sprint 1
ARAE-5	View Test Results	Evaluation Results Review	3	Core functionality; placed in Sprint 1
ARAE-6	View Rubric Score Breakdown	Evaluation Results Review	3	Core functionality; placed in Sprint 1
ARAE-7	View Total Evaluation Score	Evaluation Results Review	2	Remaining functionality; placed in Sprint 2
ARAE-8	Handle Unavailable Evaluation Results	Evaluation Status Handling	2	Remaining functionality; placed in Sprint 2

Total backlog estimate: 14 story points. Story points were assigned using relative effort and complexity, with smaller stories estimated at 2 points and more involved result-viewing stories estimated at 3 points.

Spaces

Automated Rubric Assignment Evaluator    

 Summary
  Timeline
  Board
  Backlog
  Calendar
  **List**
 Forms
  Development
  Docs
  Reports
 

 Ask AI
  Search w...
  GG
  Filter
  Group
 


☐	> Work	Assignee	Reporter	Status	Story point esti	
☐	  ARAE-1 Evaluation Results Review	 Unassigned	 Ganikhasri G	To Do ▾	None	
☐	 ARAE-3 View Evaluated Submis...	 Unassigned	 Ganikhasri G	Done ▾	2	
☐	 ARAE-4 Retrieve Evaluation Res...	 Unassigned	 Ganikhasri G	Done ▾	2	
☐	 ARAE-5 View Test Results	 Unassigned	 Ganikhasri G	Done ▾	3	
☐	 ARAE-6 View Rubric Score Brea...	 Unassigned	 Ganikhasri G	Done ▾	3	
☐	 ARAE-7 View Total Evaluation S...	 Unassigned	 Ganikhasri G	Done ▾	2	
☐	  ARAE-2 Evaluation Status ...	 Unassigned	 Ganikhasri G	To Do ▾	None	
☐	 ARAE-8 Handle Unavailable Eval...	 Unassigned	 Ganikhasri G	Done ▾	2	




 Create
 2 of 2 

3. Sprint Simulation

The lab required sprint simulation by moving work items through To Do → In Progress → Done. Two one-week sprints were completed.

3.1 Sprint 1

Story	Points	Status
ARAE-3 — View Evaluated Submissions	2	Completed
ARAE-4 — Retrieve Evaluation Results	2	Completed
ARAE-5 — View Test Results	3	Completed
ARAE-6 — View Rubric Score Breakdown	3	Completed

Sprint 1 total: 10 story points.

Search

+ Create

See plans

3+

GG

Spaces

Automated Rubric Assignment Evaluator

...

Summary

Timeline

Board

Backlog

Calendar

List

Forms

Development

Docs

+

GG

Group

Complete sprint

To Do 2

View Test Results

Evaluation Results Review

ARAE-53

View Rubric Score Breakdown

Evaluation Results Review

ARAE-63

In Progress 2

View Evaluated Submissions

Evaluation Results Review


ARAE-32

Retrieve Evaluation Results

Evaluation Results Review

ARAE-42

Done 0

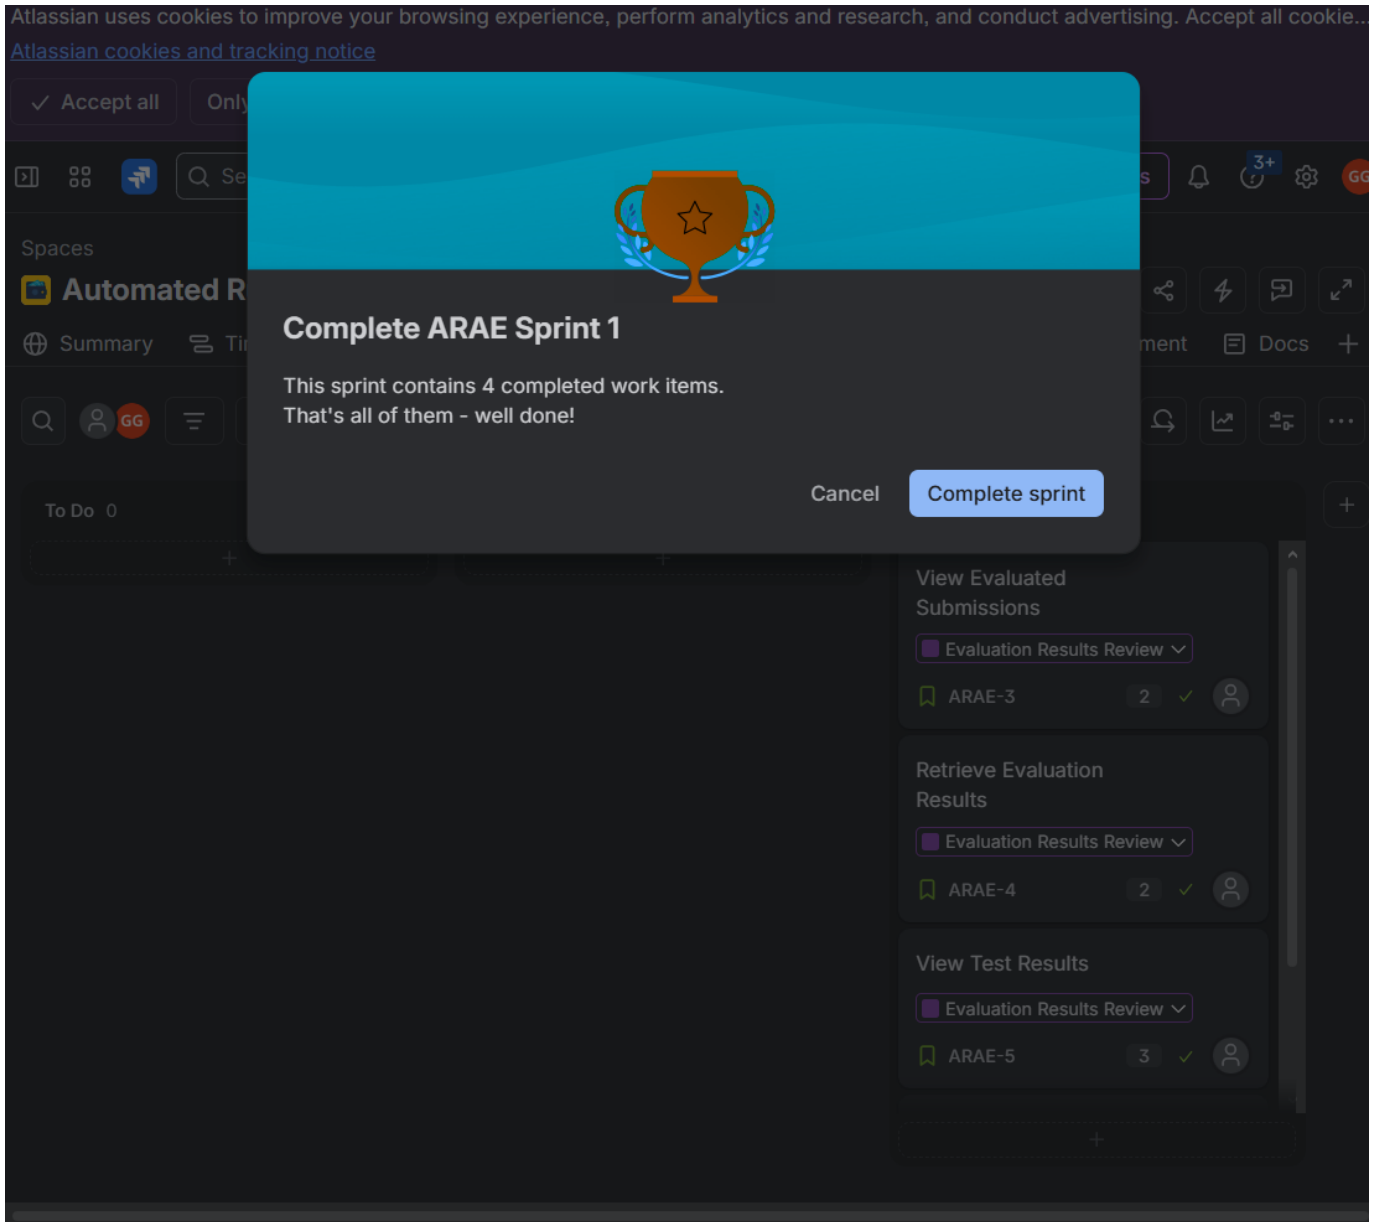

3.2 Sprint 2

Story	Points	Status
ARAE-7 — View Total Evaluation Score	2	Completed
ARAE-8 — Handle Unavailable Evaluation Results	2	Completed

Sprint 2 total: 4 story points.

Sprint goal: Complete remaining evaluation result features.

Spaces

Automated Rubric Assignment Evaluator  ...

 Summary  Timeline  **Board**  Backlog  Calendar  List  Forms  Development  Docs +

  GG   Group Complete sprint    ...

To Do 2

View Total Evaluation Score

 Evaluation Results Review

 ARAE-7 2 

Handle Unavailable Evaluation Results

 Evaluation Status Handling

 ARAE-8 2 

+

In Progress 0

+

Done 0

+

+

Spaces

Automated Rubric Assignment Evaluator  ...

 Summary  Timeline  Board  **Backlog**  Calendar  List  Forms  Development  Docs +

  GG    ...

Epic ×

 No epic

>  Evaluation Results Review ...

>  Evaluation Status Handling ...

+ Create epic

 **ARAE Sprint 3**  Add dates (0 work items) 0 0 0 Start sprint ...



Plan your sprint

Drag work items from the **Backlog** section or create new ones to plan the work for this sprint. Select **Start sprint** when you're ready.

 Describe what needs to be done.   Create ←

0 of 0 work items visible | Estimate: 0 of 0


 **Backlog** (0 work items) 0 0 0  Create sprint

Your backlog is empty.

+ Create

4. Burndown Chart

The Sprint 2 Burndown Chart was generated in Jira using Story points as the estimation field. Sprint 2 started with 4 story points and the remaining work reached 0 by completion.

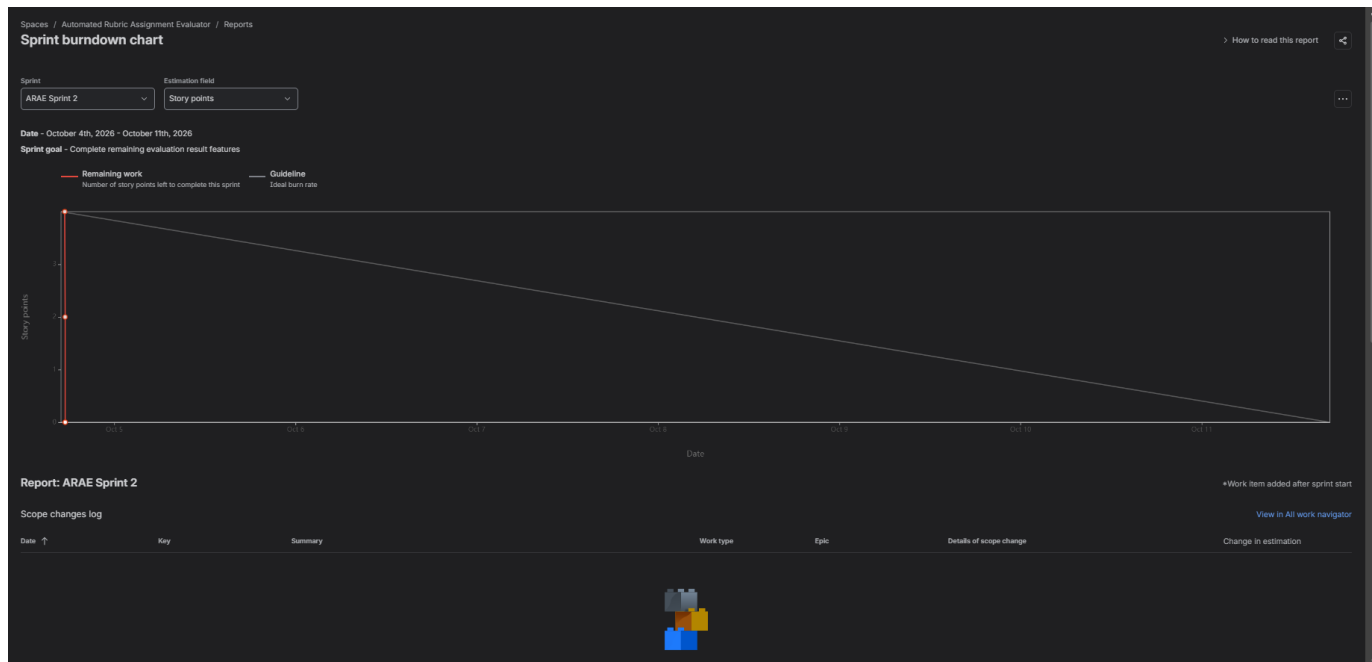

5. Reflection

5.1 Did your estimations reflect the actual effort?

Yes. Our story point estimations generally reflected the relative effort of the work. Smaller tasks such as viewing evaluated submissions, retrieving results, and viewing the total evaluation score were estimated at 2 story points, while viewing test results and the rubric score breakdown were estimated at 3 story points because they involved more information to display and review. We completed both sprints successfully, suggesting that the estimates were reasonable for our simulated workload.

5.2 Was your backlog well-prioritized?

Yes. The backlog was organized according to the importance of the Faculty Evaluator's evaluation-review workflow. The core functionality—viewing completed submissions, retrieving evaluation results, viewing test results, and viewing the rubric breakdown—was placed in Sprint 1. The remaining functionality, viewing the total score and handling unavailable results, was completed in Sprint 2. This allowed the main evaluation-review features to be addressed first.

5.3 How did your simulated sprint align with your plan?

The simulated sprints followed the planned backlog successfully. Sprint 1 contained four stories totaling 10 story points, while Sprint 2 contained two stories totaling 4 story points. The stories were moved through To Do → In Progress → Done, and both sprints were completed without unfinished work. The Sprint 2 burndown chart also shows the remaining work decreasing from 4 story points to 0.

5.4 What insights did the burndown chart give about your team's capacity?

The burndown chart showed that the team completed the planned 4 story points in Sprint 2. The remaining work decreased to zero, indicating that the sprint goal was achieved. Since this was a simulated sprint where tasks were moved through the workflow quickly, the burndown was much faster than a typical real-world sprint. In a real project, the chart could be used to identify whether the team was progressing at the expected rate and whether the sprint goal was at risk.
