

SE LAB-2

Name: Gagana C

SRN: PES1UG24AM099

Section: B

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Project: Automated Rubric Assignment Evaluator (Jira project 'epics', key EP, Scrum board)

1. Epics

Epic	Name	Description	Stories	Points
EP-1	Epic 1: Project Submission	Allow students to upload project ZIP files for automated evaluation.	2	5
EP-2	Epic 2: Automated Evaluation & Scoring	Queue submissions, run syntax checks and unit tests, and generate itemized rubric score breakdowns.	4	26
EP-3	Epic 3: Peer Review & Results	Assign projects to peer reviewers automatically and let students and faculty view test results and rubric scores.	3	13

2. User Stories, Priority and Story Points

Key	Story	Epic	Priority	Points	Sprint
EP-4	Story 1.1: Upload ZIP	Epic 1	High	3	Sprint 1
EP-5	Story 1.2: Upload Confirmation	Epic 1	High	2	Sprint 1
EP-6	Story 2.1: Queue Submissions	Epic 2	High	5	Sprint 1
EP-7	Story 2.2: Run Syntax Checks and Unit Tests	Epic 2	High	8	Sprint 1
EP-8	Story 2.3: Generate Rubric Score	Epic 2	High	8	Sprint 1
EP-9	Story 2.4: Handle Load and Response Time	Epic 2	High	5	Sprint 2
EP-10	Story 3.1: Auto-Assign Peer Reviewer	Epic 3	High	8	Sprint 2
EP-11	Story 3.2: Student Views Results	Epic 3	Medium	3	Sprint 2
EP-12	Story 3.3: Faculty Views Results	Epic 3	Medium	2	Sprint 2

Total: 9 user stories, 44 story points (Fibonacci scale).

3. Jira Backlog with Epics and User Stories

For you

Recent

Starred

Apps

Plans

Spaces

Recent

epics

Recent

EP board

My Software Team

More spaces

Recommended

Create a roadmap

Filters

Search work items

Default filters

My open work items

Reported by me

All work items

Open work items

Done work items

Viewed recently

Created recently

Resolved recently

Spaces / epics

EP board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Search backlog

Version

Epic

Quick filters

Create

No epic

Epic 1: Project Submission

Key

EP-1

Work items

2

Completed

0

Estimate

5 points

0% of estimated work complete

0 work items unestimated

View details

Create work item

Epic 2: Automated Evaluation & Scoring

Key

EP-2

Work items

4

Create epic

Backlog (9 work items)

Create a whiteboard to plan your work

EP-4 Story 1.1: Upload ZIP

Epic 1: Pr...

To Do

3

EP-5 Story 1.2: Upload Confirmation

Epic 1: Pr...

To Do

2

EP-6 Story 2.1: Queue Submissions

Epic 2: Au...

To Do

5

EP-7 Story 2.2: Run Syntax Checks and Unit Tests

Epic 2: Au...

To Do

8

EP-8 Story 2.3: Generate Rubric Score

Epic 2: Au...

To Do

8

EP-9 Story 2.4: Handle Load and Response Time

Epic 2: Au...

To Do

5

EP-10 Story 3.1: Auto-Assign Peer Reviewer

Epic 3: Pe...

To Do

8

EP-11 Story 3.2: Student Views Results

Epic 3: Pe...

To Do

3

EP-12 Story 3.3: Faculty Views Results

Epic 3: Pe...


To Do

2

Create

Backlog showing all 9 user stories linked to their Epics, with priority and story points.

4. Story Point Assignments

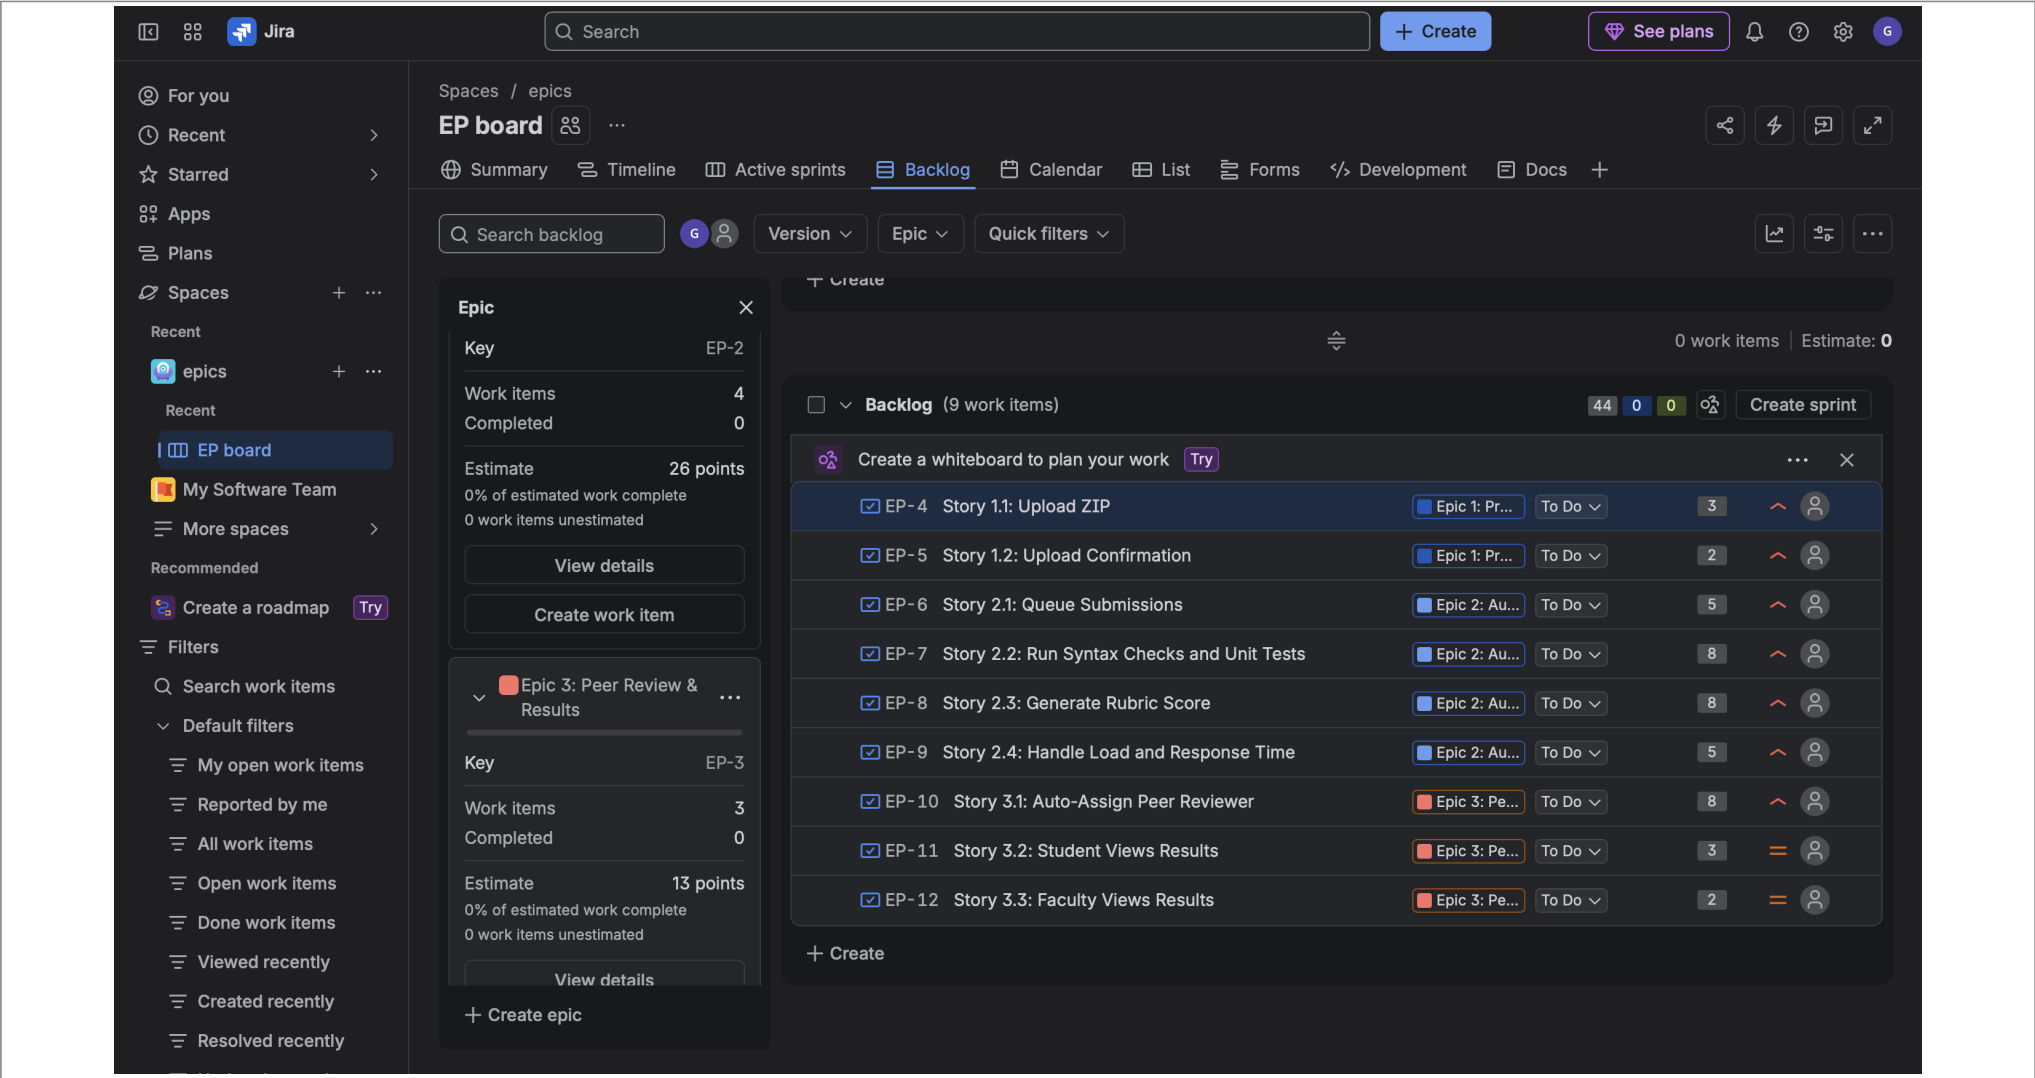


Story points on every story (Fibonacci scale). Epic panel totals: Epic 1 = 5, Epic 2 = 26, Epic 3 = 13 points.

5. Sprint Summary

Sprint	Stories	Points committed	Points completed	Planned duration	Actual time taken
EP Sprint 1	1.1, 1.2, 2.1, 2.2, 2.3	26	26	1 week	About 5 minutes (simulated)
EP Sprint 2	2.4, 3.1, 3.2, 3.3	18	18	1 week	About 5 minutes (simulated)


Sprint 1 goal: Accept submissions, run automated tests and generate rubric scores. Sprint 2 goal: Handle load, assign peer reviewers and let users view results.

Sprint 1: Active Sprint Board

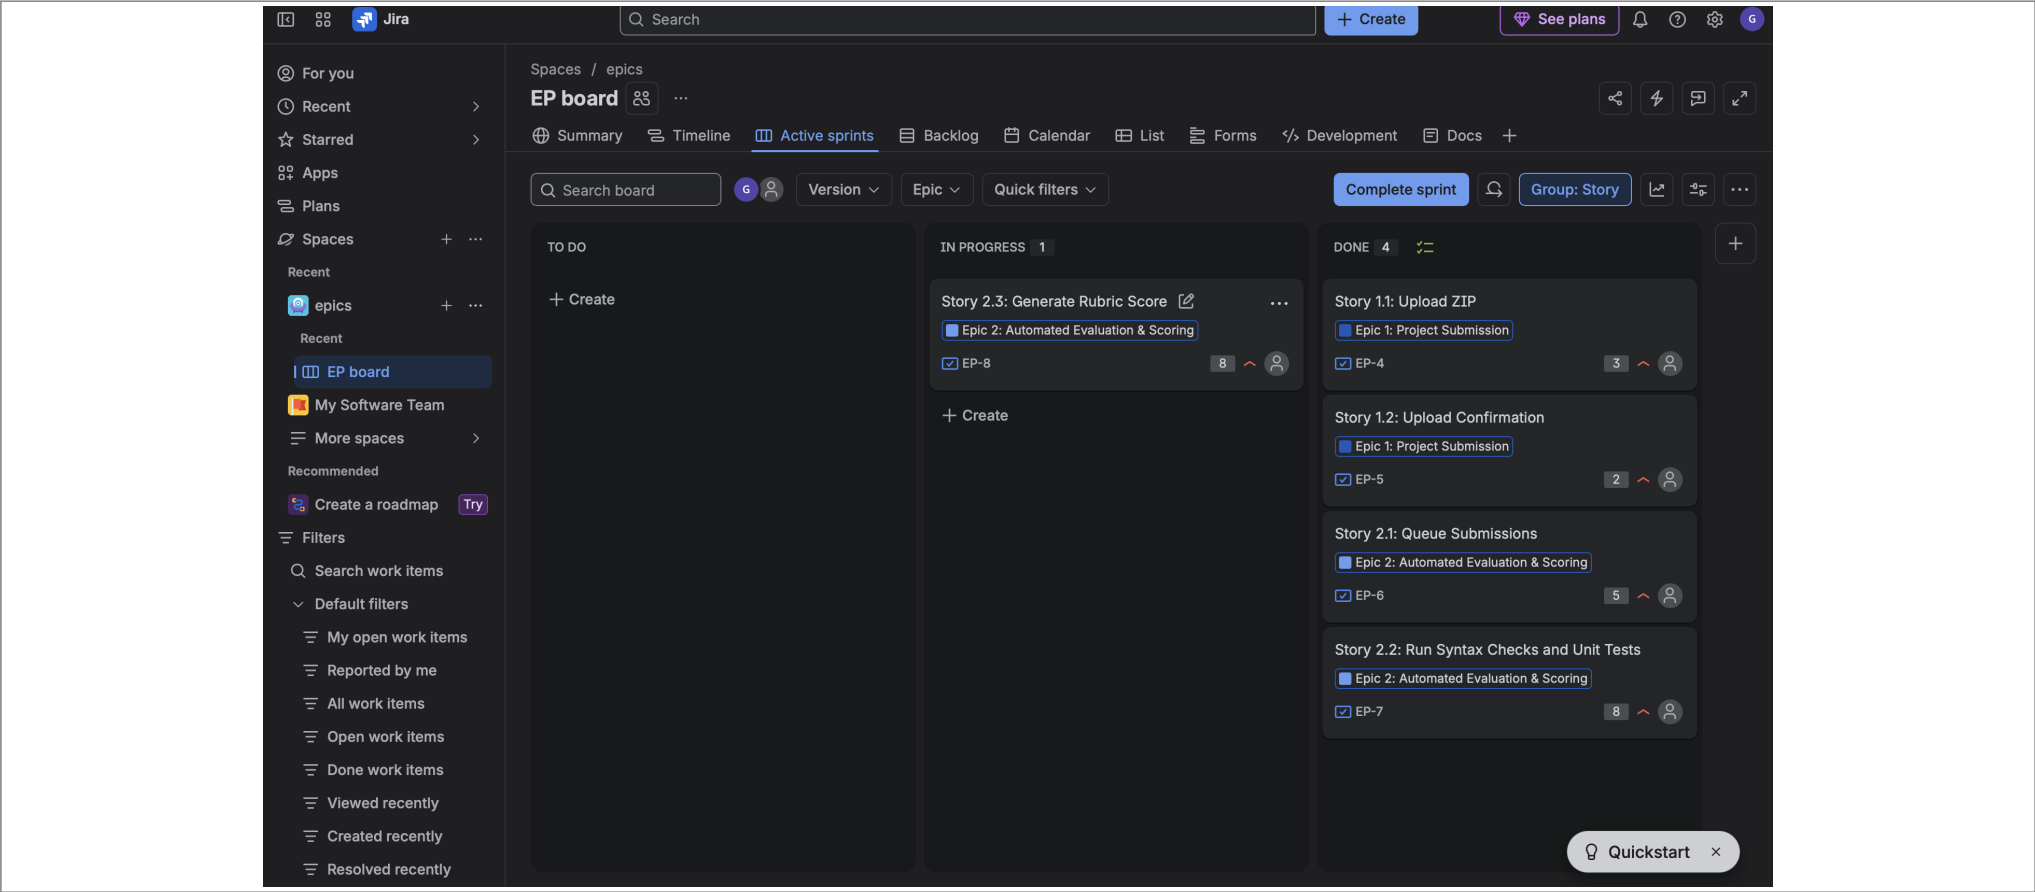


Sprint 1 board with cards across In Progress and Done.

6. Burndown Chart: Sprint 1

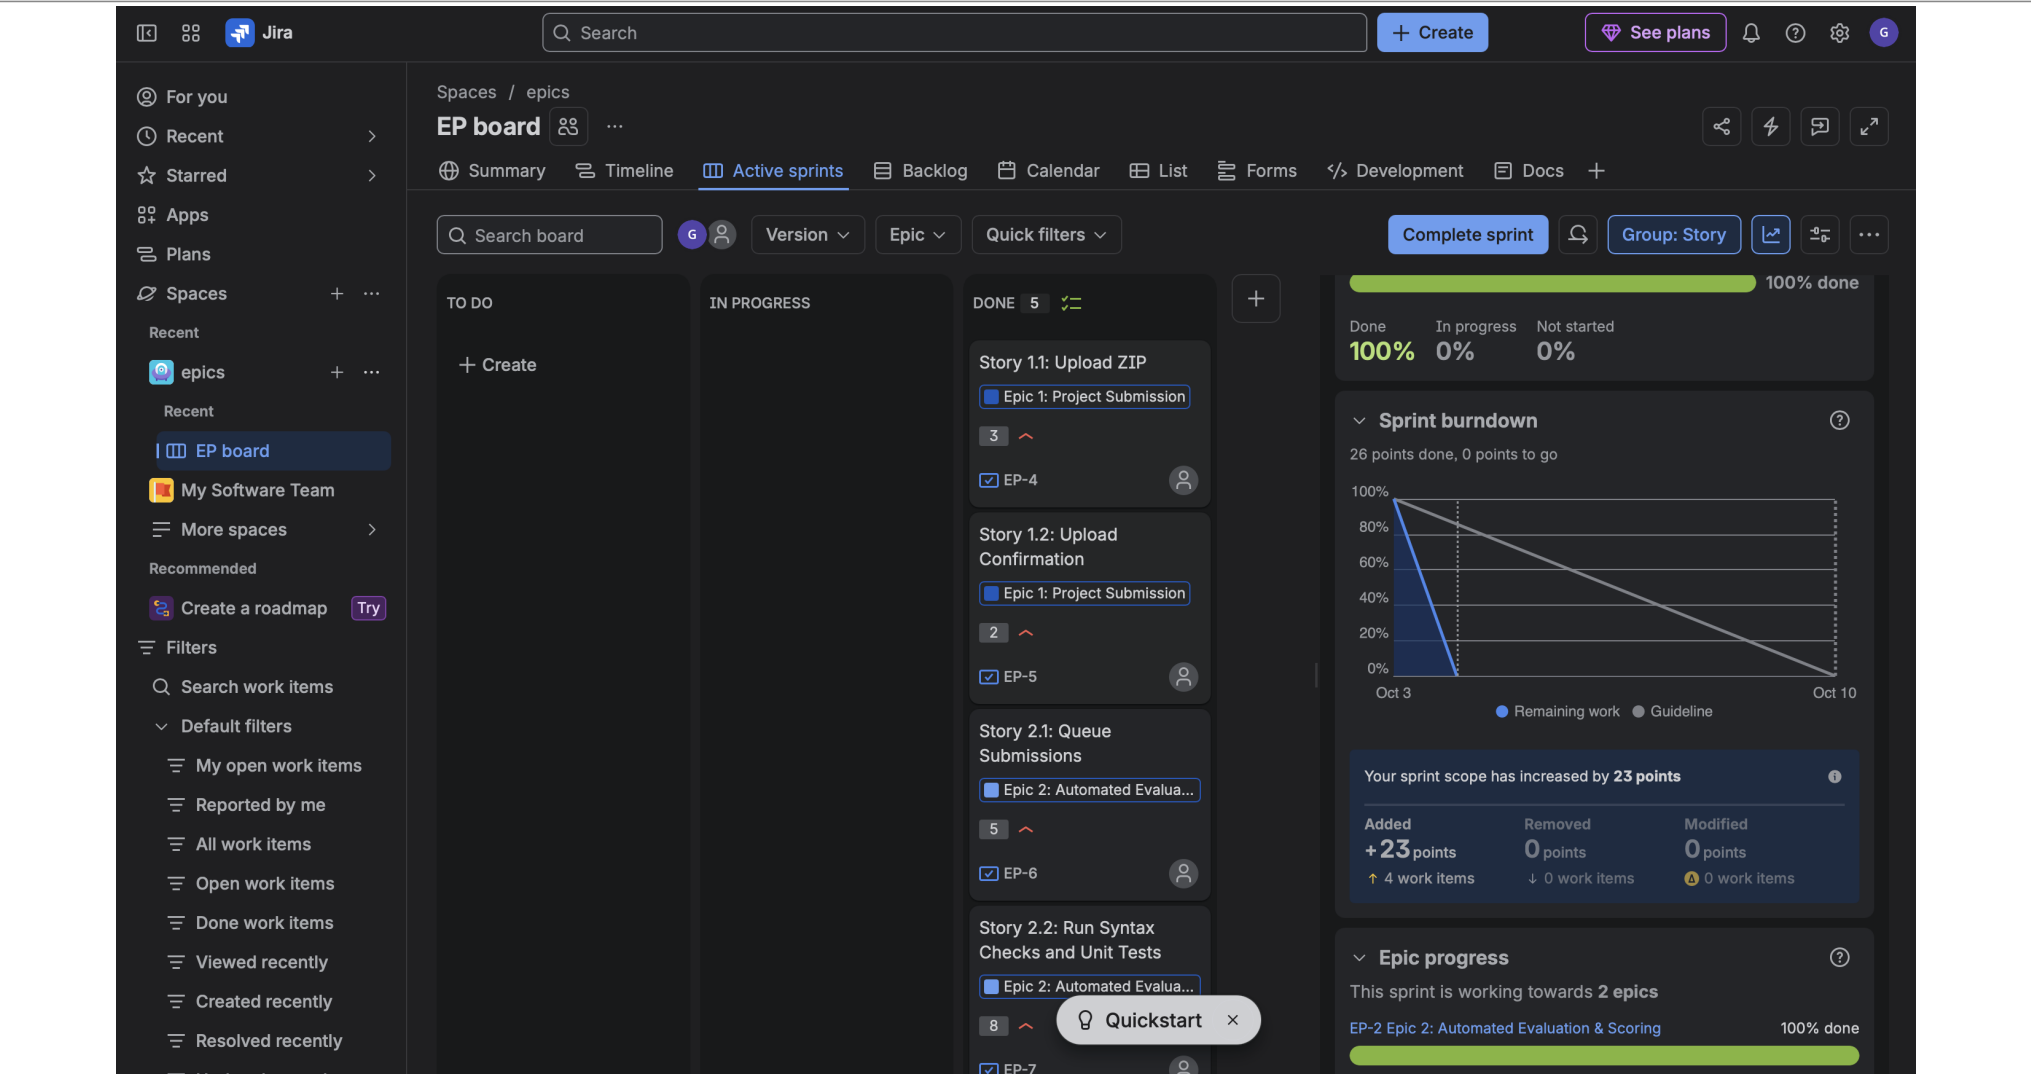


Sprint 1 burndown: 26 points done, 0 to go. The remaining-work line (blue) falls steeply below the guideline (grey).

7. Sprint 2: Active Sprint Board

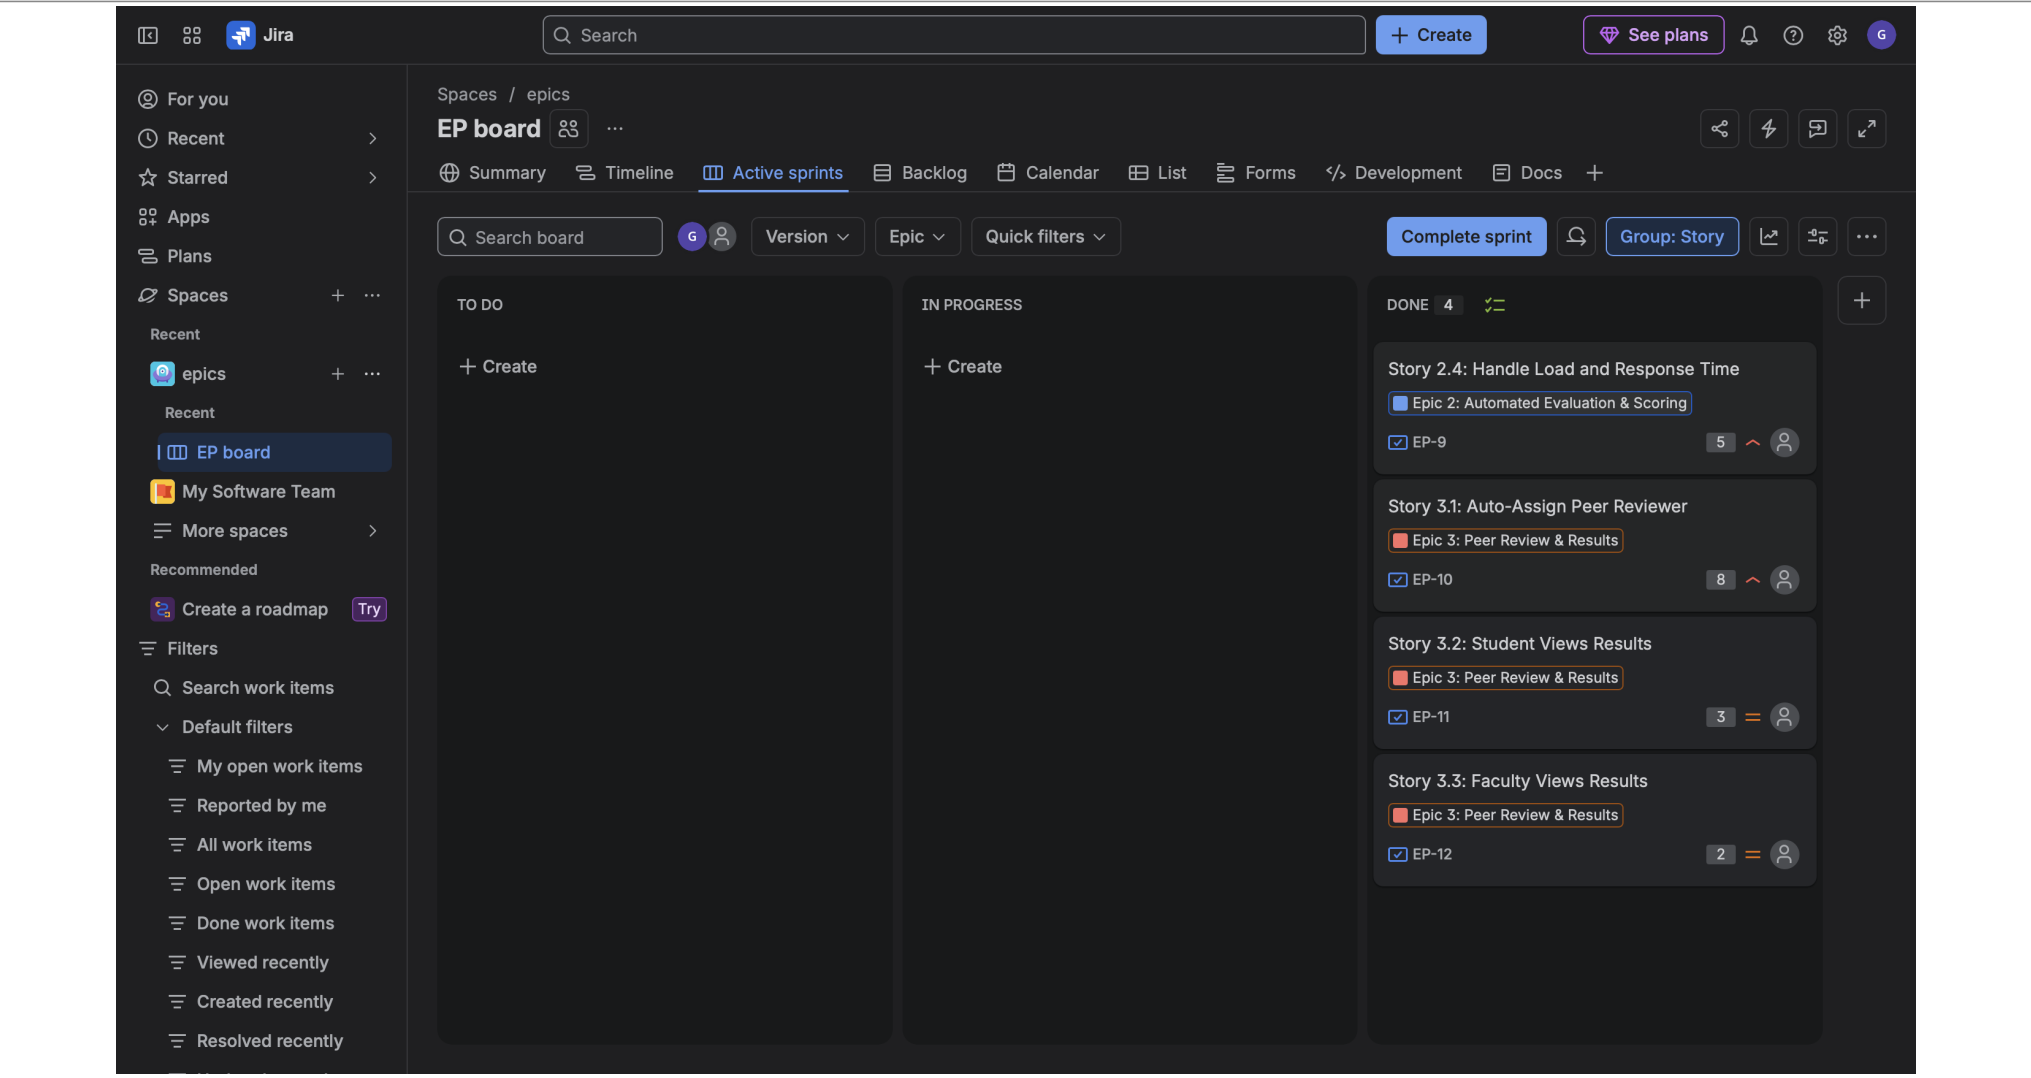

Sprint 2 board with all 4 stories in Done.

8. Burndown Chart: Sprint 2

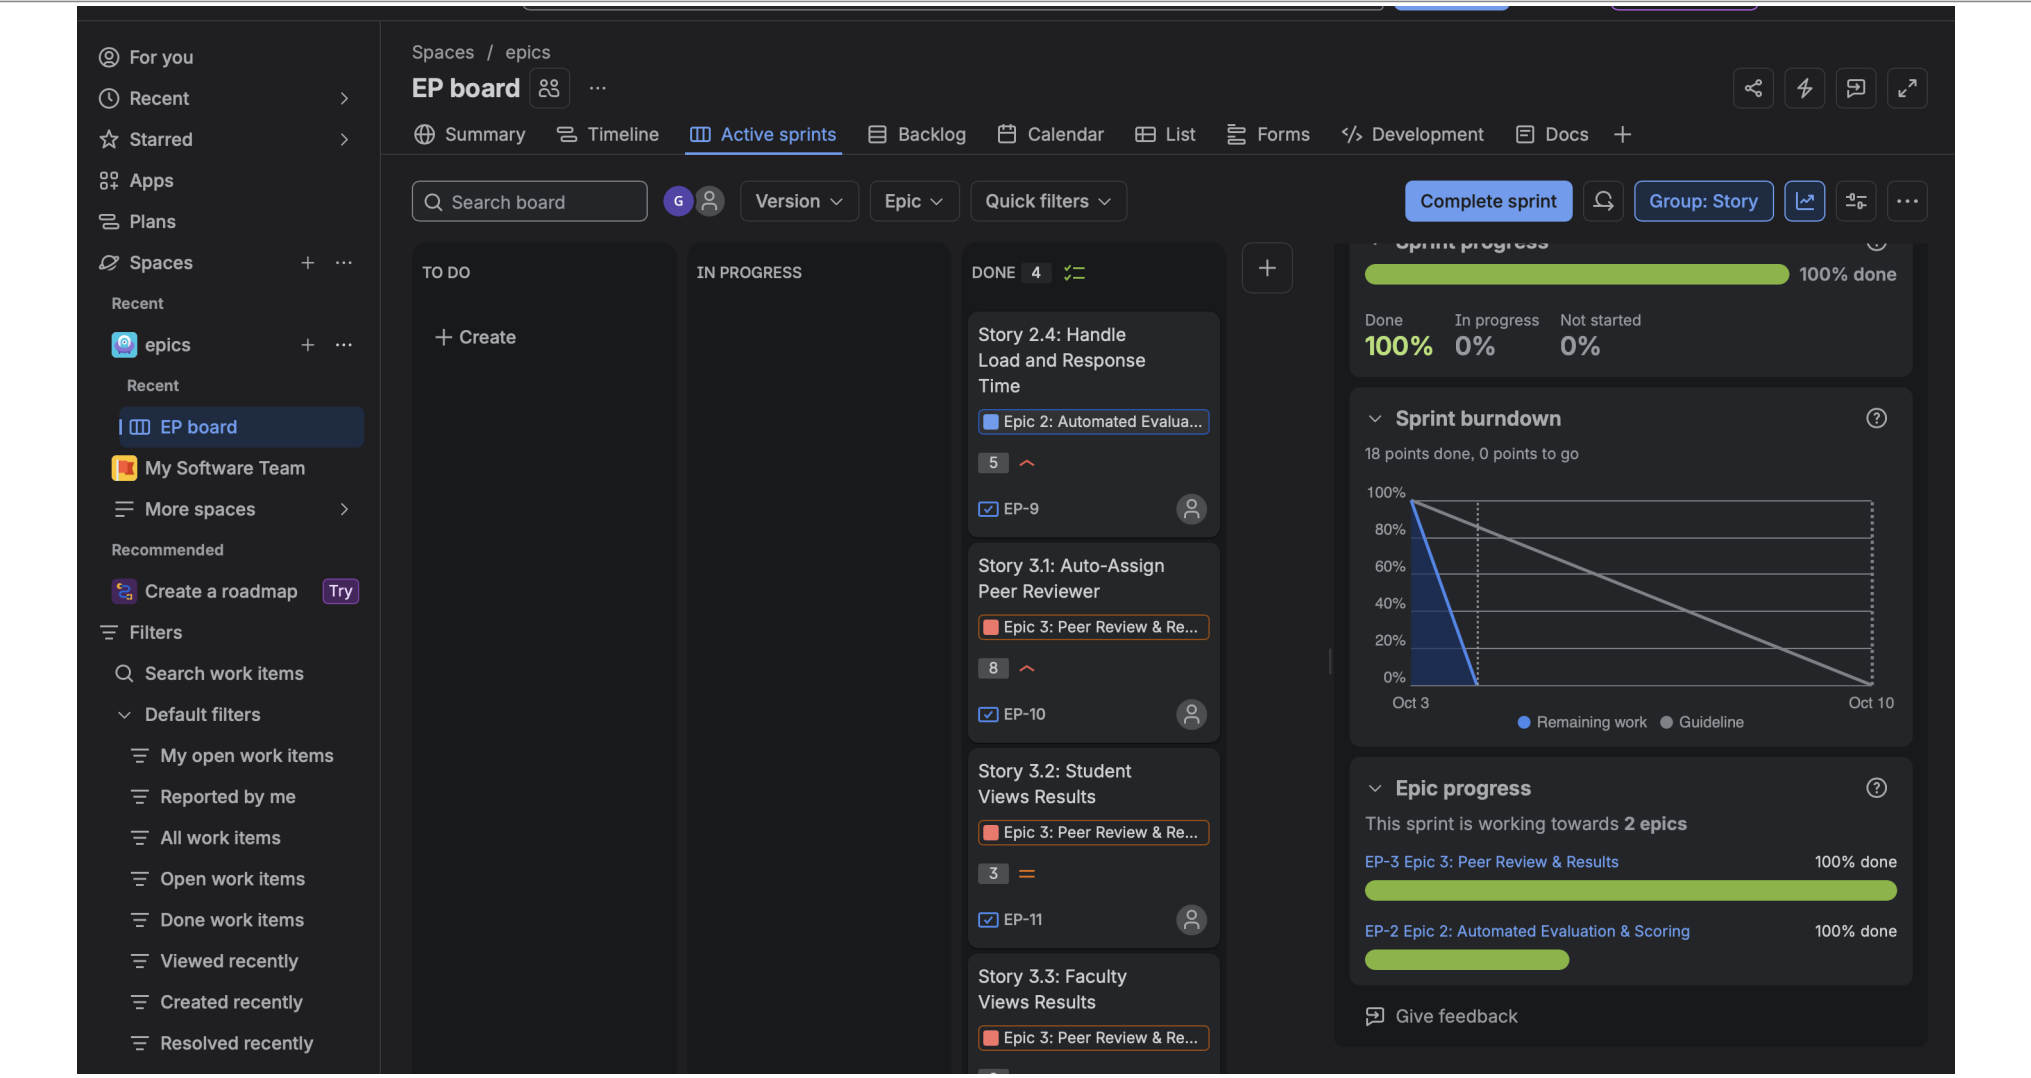

Sprint 2 burndown: 18 points done, 0 to go. Both Epic 2 and Epic 3 show 100% done in Epic progress.

9. Reflection

1. Did your estimations reflect the actual effort?

Partly. I worked alone, so Planning Poker was not possible. I estimated each story myself by comparing complexity, amount of work and uncertainty, and I gave the largest values (8 points) to running syntax checks and unit tests, generating the rubric score and auto-assigning peer reviewers, because they involve the most logic and risk. Small, well-understood stories such as upload confirmation and faculty view got 2 points. All 9 stories were finished inside their sprints without re-estimating, so the sizes were workable. However, because the sprints were simulated by dragging cards, I did not measure real effort, so I cannot confirm how accurate the numbers really were. With a team, Planning Poker would expose differing views and give a more reliable estimate.

2. Was your backlog well-prioritized?

Yes. The core workflow stories (upload, queue, syntax and unit tests, rubric scoring) are High priority and were placed in Sprint 1, because everything else depends on them. Story 2.4 (load and response time) and Story 3.1 (peer review assignment) are also High but were scheduled in Sprint 2, since they only make sense once the main pipeline works. The two results-viewing stories are Medium because they present data that the earlier stories produce. Overall the order followed business value and dependencies.

3. How did your simulated sprint align with your plan?

Both sprints matched the plan exactly. Sprint 1 committed 26 points and completed 26. Sprint 2 committed 18 points and completed 18, so no stories were carried over and the backlog ended empty. The sprints were planned for 1 week each, but I moved the cards across To Do, In Progress and Done in about 5 minutes per sprint, so there were no delays or blockers as there might be in a real project.

4. What insights did the burndown chart give about your team's capacity?

In both sprints the remaining-work line dropped very steeply and finished well below the grey guideline. This is not real capacity. It happened because every card was completed within minutes of the start of a one-week sprint. In a real team, a sharp drop like this can mean work was not updated evenly, stories were too large or poorly broken down, or too little was committed. The chart does show my velocity: 26 points in Sprint 1 and 18 in Sprint 2 (44 total). I would use these as a rough baseline, but a real team would need several sprints of genuine work before trusting them for planning.
